



WEEK 8 – GOVERNANCE AND IMPLEMENTATION STRATEGY DOCUMENT

End-to-End Salesforce CRM Transformation for Customer Operations
and Service Management

8.1 Governance Framework

To safeguard GreenGrid Utilities' new Salesforce ecosystem against data corruption, unauthorized configuration changes, and technical debt, a formal governance structure is established. This framework preserves the configuration-first philosophy (**Milestone 3**) and role-based access parameters (**Milestone 5**).


8.1.1 Center of Excellence (CoE) Structure

A cross-functional Center of Excellence (CoE) is formed to review platform health, prioritize enhancement requests, and audit security compliance weekly.

- **Executive Sponsor (Executive Management Tier):** Ensures platform alignment with overarching business goals (**BR1–BR3**).
- **Business Change Lead (Customer Support/Field Operations Managers):** Validates that proposed technical changes map accurately to frontline workflows.
- **System Administrator (IT Tier):** Acts as the primary platform gatekeeper, managing security settings, user provisioning, and flow optimization.

8.1.2 Environment and Release Management Strategy

To maintain the required 99.9% platform availability (**NFR1**), direct configuration changes in the Production environment are strictly prohibited. A multi-sandbox release pipeline is implemented:

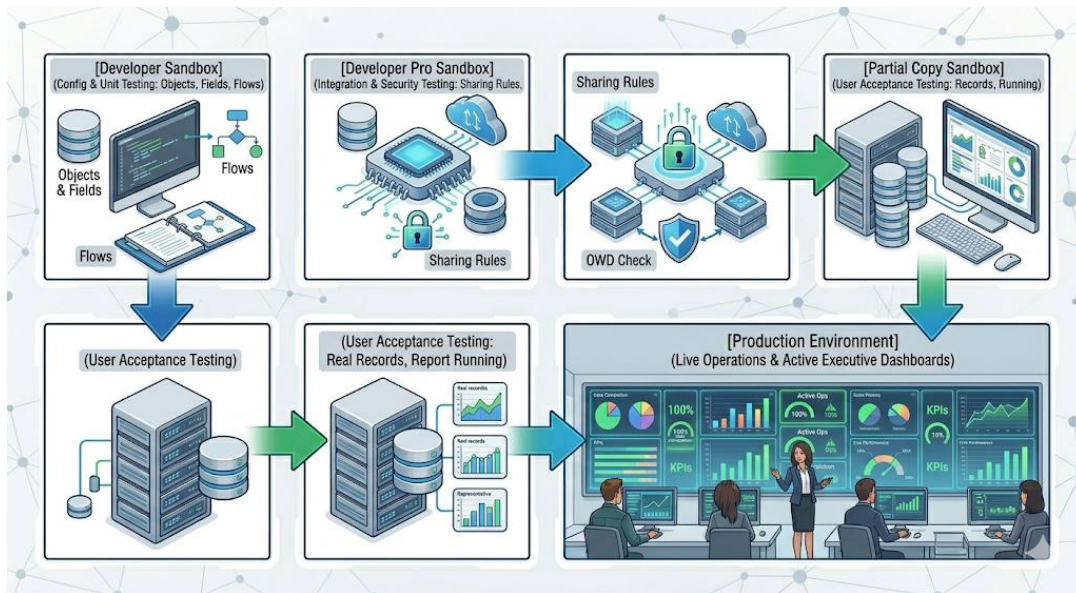

8.1.3

Change Control Board (CCB) Protocols

Any modification to critical data objects (Utility_Asset__c, Field_Visit__c) or core automation flows (**Flow 1 & Flow 2**) must clear a formal three-tier assessment before deployment:

1. **Risk Analysis:** Does the change impact the sub-2-second Meter ID indexed search target (**FR1**)?
2. **Security Review:** Does it breach the Private Organization-Wide Default (OWD) baseline (**Milestone 5**)?
3. **Rollback Planning:** A documented rollback script must be prepared to revert configuration states in Production within a 15-minute window if unexpected errors occur.

8.2 User Adoption Strategy

Moving from a fragmented spreadsheet environment to a centralized CRM requires a structured change management strategy to minimize frontline friction and eliminate data latency (**B3**).

8.2.1 Role-Based Training Programs

Training cannot be generic; it must be tailored directly to the distinct user experiences engineered across Milestones 5, 6, and 7.

Customer Support Track

Hands-on simulations focusing exclusively on the unified **Service Console**. Agents practice answering calls, executing high-speed Meter ID lookups (**FR1**), and saving high-priority cases to trigger the background dispatch engine.

Field Operations Track

Mobile-only training sessions on smartphones. Technicians practice logging into the **Salesforce Mobile App**, receiving real-time push alerts, updating Repair_Status__c to "Resolved", and inputting Technician_Notes__c to ensure zero paperwork loss.


8.2.2 Adoption Metrics and Gamification

Leadership tracks deployment success using native Salesforce reports focused on three core adoption categories:

- **Login Frequency:** Checking that 100% of provisioned support agents and field workers log in daily.
- **Data Completeness Rate:** Auditing closed cases to verify that Technician_Notes__c are recorded without placeholders or empty strings.
- **Dashboard Engagement:** Monitoring how frequently management teams access the Executive Operations Dashboard to drive operational decisions.

8.3 Implementation Plan

The deployment of the GreenGrid Utilities Salesforce platform follows a structured, phased rollout schedule over a 6-week timeline to minimize operational disruption.

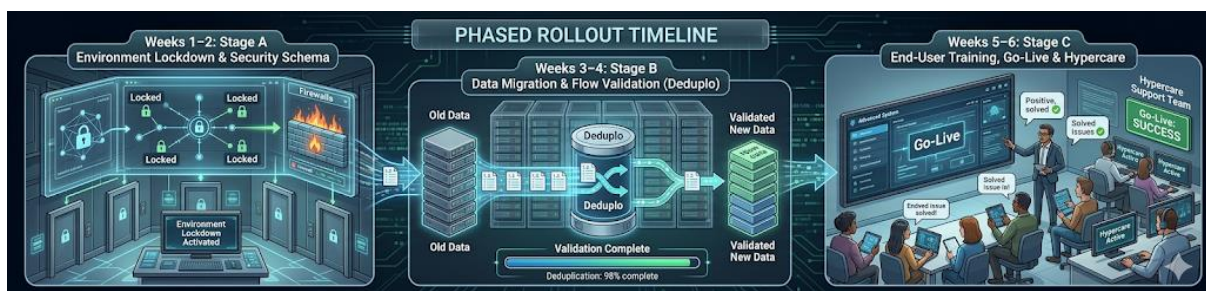

Stage A: Environment Lockdown & Security Baseline (Weeks 1–2)

Provisioning metadata schema, locking down Private OWDs, establishing the Role Hierarchy, and validating permission sets in lower sandboxes.

Stage B: Data Migration & Automation Validation (Weeks 3–4)

Extracting legacy Excel customer tables, indexing Meter IDs, running platform deduplication routines, and deploying **Flow 1** and **Flow 2** structural logic.

Stage C: User Training, Go-Live, & Hypercare Support (Weeks 5–6)

Executing end-user training, pushing verified change sets to Production, running live smoke tests, and providing 24/7 dedicated support desk hypercare during week 1 of active deployment.

Conclusion

With the completion of **Milestone 8: Governance and Implementation Strategy**, GreenGrid Utilities has established a clear path to go-live.

By implementing a multi-sandbox pipeline, an administrative Change Control Board, role-specific onboarding plans, and native change-tracking tools, the platform protects its data core.

This final strategy guarantees that the Salesforce implementation delivers immediate, lasting business value while maintaining 99.9% operational availability from day one.
